

Dealership:
Technician:
Customer Name:
Model:
Serial #:
Estimated Setup Time: 3 hours



Safety:

- ☐ Operator's manual located in the designated holder.
- ☐ Ensure all safety decals are in place and legible.
- ☐ Safety locks are functional and in place.
- ☐ Safety chain inspection (refer to manual).
- ☐ Safety lights and slow moving vehicle sign are functional and visible.

Check List:

(Refer to operator's manual for instructions).

- ☐ Remove TOP GUN® joystick control or control box with harness located in the auger transition housing. (Fig.1).
- ☐ Remove shipping blocks.
- ☐ Wash the unit, removing all road debris (road salt and other material).
- ☐ Check for aesthetic defects and shipping damage – replace damaged items or touch up paint as required.
- ☐ Check wheel bolts, as per operator manual specifications.
- ☐ Check tire pressure and adjust as required.
- ☐ Check oil level in gearbox.
- ☐ Verify machine has been greased as per operator manual specifications.
- ☐ Remove safety lock and driveline from shipping position. Remove shipping bracket. Install PTO and safety lock. (Fig.2).

- ☐ Remove the forks and install, retain lock nut and bolt (Fig.3). Discard shipping brackets and nut. (Forks will have to be swapped side to side on Twine Sickle™ equipped models).
- ☐ Remove discharge chute from shipping location and set aside. (Fig.4)
- ☐ Support turret assembly, remove shipping brackets and rotate turret assembly into working position and secure. Discard shipping brackets. Fig.5 & Fig.6
- ☐ Install discharge chute on turret.
- ☐ Relocate jack from the shipping location on the fan assembly to the hitch Fig.7
- ☐ Fold side shields into place and fasten. Install front screen. (This may be already done depending on shipping configuration, see photo on last page).
- ☐ Open guard in rear of machine and verify auger belt tension.
- ☐ Open guard in front of machine and verify blower fan belt tension.
- ☐ Ensure all manual operated adjustments function properly and freely.
- ☐ Verify feed rollers are set to low on RHS and high to LHS (Front and rear).

Completed:	Signature:	Date:

Operational Check:

- ☐ Cycle all hydraulic functions. Verify all functions operate correctly. Check for any leaks. ****Note, when connecting joystick to machine for operational tests ensure implement connection is connected first before power is connected to joystick or a controller error will result.**
- ☐ Engage PTO, ensure operation.
- ☐ Verify TOP GUN™ clutch operation.
- ☐ Cycle test the Twine Sickle™ (optional equipment)

Customer Review:

- ☐ Review with the customer the understanding and operation of the machine.
- ☐ Review with the customer the safety section of the operator's manual.

Comments:

Support Pictures:

Figure 1.

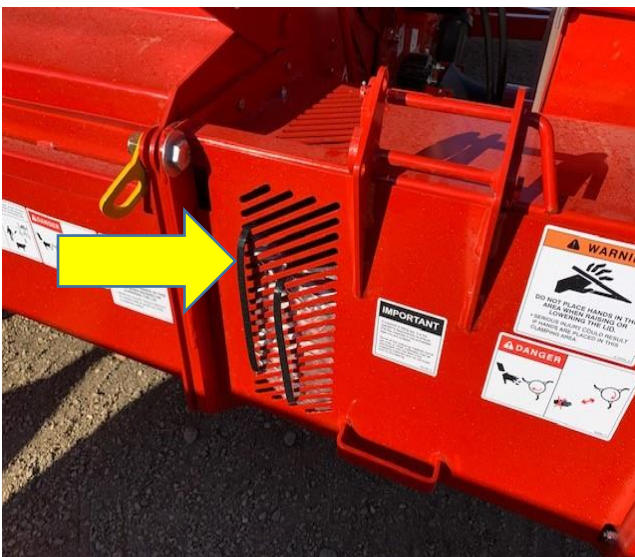


Figure 2.



Figure 3.

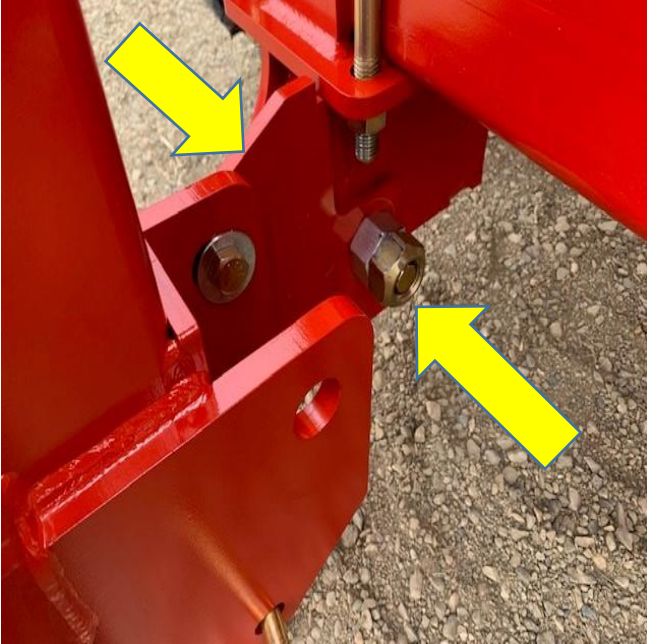


Figure 4.



Figure 5.



Figure 6.



Figure 7.



NOTE: TOP DECK SHIPPING

